

Record Number: WSR21-0030 Septic Site Address: 9470 Riverside Dr Jenner

Inspector: Lindsay Segbers Hall


Date: 4/6/2022

| Fraction Conversion | | | | | |
|---------------------|------------------|-----------------|--|--|--|
| 1/8 inch= 0.125 | 1/2 inch =0.500 | 7/8 inch= 0.875 | | | |
| 1/4 inch=0.250 | 5/8 inch=0.625 | | | | |
| 3/8 inch =0.375 | 3/4 inch = 0.750 | | | | |

Limiting Condition is the measurement to the ground water. If it is a dry hole, limiting condition is the bottom of the hole.

| Ground Water Test Readings | | | | | | |
|----------------------------|---|------------------------------------|-------------|------------|---------|--|
| GW Hole # | Measurement from Top of the Pipe to Limiting conditions | Top of pipe to ground (surface) | Depth to GW | WET or DRY | Remarks | |
| 1 | 63.75 | 26.375 | 37.375 | Dry | | |
| 2 | 116.25 | 37 | 79.25 | Dry | | |
| 3 | 118.75 | 24.125 | 94.625 | Dry | | |
| 4 | 117.25 | 26.125 | 91.125 | Dry | | |
| 5 | 114.625 | 19.875 | 94.75 | Dry | | |
| | | | | N/A | | |
| | | | | N/A | | |
| | | | | N/A | | |
| | | | | N/A | | |
| | | | | N/A | | |



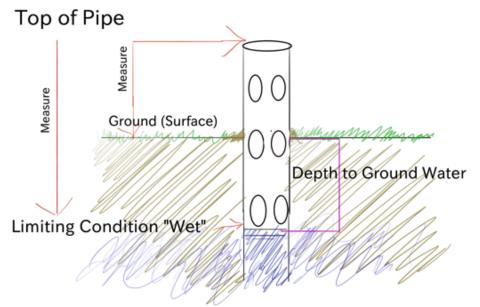

***If there is no pipe, measure from the ground surface to limiting conditions.
